

*****Draft Document Only.Task is not yet Completed/Approved.*****

Ref :20260619163255

Date :23-Jun-2026

TASK DETAILS

Site ID : ZKAD16 Site Name : Ganemulla_Camp
Report Category : T S S R B T S5 G Z T Performed By : ZTE

Project Details		
No	Task	Status
1.1	Project Name	5G Expansion Phase 1
1.2	Implementation By	ZTE
1.3	TSSR Type	ZTE 5G
1.4	Project Scope	Swap
1.5	Site Officer	Mr. Asanka Herath
1.6	Vendor Group	ZTE
1.7	Sub-Contractor Company	Fame Global Solutions
1.8	Sub-Contractor Officer	Mr. Nadith Priyan
1.9	Site Survey Date	2026-06-19
1.10	Site Officer Contact No	0704289579
Site Info		
No	Task	Status
2.1	Address	12/4,_Maharanugegoda,_Kadawatha.
2.2	Longitude	79.9596
2.3	Latitude	7.0287
2.4	Altitude	
2.5	Existing Technology	2G 4G

2.6	Frequency Band	G900 L1800 L2100 L2600
Site Acc Info		
No	Task	Status
3.1	Operator	Mobitel
3.2	Site Owner Name	
3.3	Site Owner Contact Number	
3.4	Access Restriction	Yes
3.5	Access Restriction Remarks	Need to inform Mobitel region officer before access to site
3.6	Access on 7 Days	Yes
3.7	Access on 7 Days Remarks	Need to inform Mobitel region officer before access to site
3.8	Access on 24 Hours	Yes
3.9	Access on 24 Hours Remarks	Need to inform Mobitel region officer before access to site
3.10	Prior appointment for access (person to be informed before site access)	Yes
3.11	Prior appointment for access Remarks	Need to inform Mobitel region officer before access to site
3.12	Contact Person	Mr. indrajith
3.13	Contact Number	0714720071
3.14	Site access key	Mobitel Access Key
3.15	Parking space available	Yes
3.16	Equipment Delivery	Hand
3.17	Safe access to all equipment parts And antennas (lifeline systems, fall arrest systems, anchors.)	Yes
Site Env Info		
No	Task	Status
4.1	Equipment Location	Roof Top
4.2	Building Floor No	

4.3	Equipment Cabinet	Outdoor Cabinet					
4.4	Evidence of Flooding	No					
4.5	Distance to Site from Colombo	Less than 50km					
4.6	Distance to Site from Colombo (Km)	27					
Manual Transport GF							
No	Name	Total Distance(m)	Steep Terrain (m) Less than 45Deg	Steep Terrain (m) Greater Than 45Deg	Terrain Condition (m)Flat	Terrain Condition (m)Rocky	Terrain Condition (m)Hill
1	Green Filed manual handling (m)	N/A	N/A	N/A	N/A	N/A	N/A
Tower Info							
No	Task	Status					
6.1	Tower Type	1_MP					
6.2	Tower Leg Type	Any special remark of tower Leg					
6.3	Tower Height	7					
6.4	Spare Antenna Poles	Yes					
6.5	Spare Antenna Poles Count	0					
6.6	Spare Plinth Availability	No					
6.7	Spare Plinth Count	0					
6.8	Spare Plinth type	N/A					
6.9	Tower Section Additional Remarks						

Tower Section Images1		Tower Section Images2
Tower Section Images3		
Power Info Mobitel		
No	Task	Status
7.1	Meter Cubical installed	Yes
7.2	Meter Cubical owner	Mobitel
7.3	Existing Commercial Power Source (Mobitel)	Three phase
7.4	Power Source Type	Mobitel CEB
7.5	Mobitel SPD Available Location	near ACDB
7.6	Power cable length between Mobitel meter cubical to Mobitel ACDB	35
7.7	Power cable length between mobitel ACDB to SLT eNodeB	10
7.8	Existing Free Breaker Qty in mobitel ACDB	3
7.9	Existing Free Breaker Capacity in mobitel ACDB	32A*1, 16A*2
7.10	ECB available at Mobitel meter cubical	No
7.11	Remarks on Mobitel Power Info	
Mobitel Power images 1		Mobitel Power images 2
Mobitel Power images 3		
Power Info SLT		
No	Task	Status
8.1	Meter Cubical installed	No
8.2	Meter Cubical owner	Mobitel
8.3	Existing Commercial Power Source (SLT)	Three phase
8.4	Power Source Type	Mobitel CEB
8.5	Power cable length between meter cubical to SLT SPD	35
8.6	Existing AC Power Cable Type	4 * 16 Non Armered

8.7	Accessories in existing SLT SPD enclosure box details (For Outdoor sites only)	SPD
8.8	SLT existing DCDB availability in 19 Inch Rack	
8.9	ECB available at SLT meter cubical	NA
8.10	ECB available at existing SLT plinth	Yes
8.11	ECB available (Indoor site only)	NA
8.12	Remarks on SLT Power Info	AC power shared from Mobitel ACDB
SLT Power images 1		SLT Power images 2
SLT Power images 3		
TX Info SLT		
No	Task	Status
9.1	TX fiber availability to the site - SLT	Yes
9.2	SLT ODF location	N/A
9.3	Remarks on SLT TX Info	TX shared from Mobitel
9.4	Remarks on Mobitel TX Info	ODF in Mobitel cabinet 3
SLT TX images 1		SLT TX images 2
SLT TX images 3		
TX Info Mobitel		
No	Task	Status
10.1	Mobitel TX Mode	Fiber
10.2	TX fiber availability to the site - Mobitel	Yes
10.3	Mobitel ODF location	Inside cabinet
10.4	Mobitel SSR availability	Yes
10.5	Distance between Mobitel CSR and SLT BBU	4



Mobitel TX images 1						Mobitel TX images 2					
Mobitel TX images 3											
Manual Transport Special											
No											
1											
2											
3											
4											
5											
Cabinet Info											
No	Cabinet No	Cabinet Type	Rectifier type	Rectifier Qty	DC Voltage	Spare Breaker Qty	Spare Breaker Capacity	Battery Type	Battery Physical Condition	Battery Capacity	Battery Qty
	Cabinet 01	TP4820 0A	R4850-1 U	2	51.1	3	63A*1, 16A*2	ZTE_LI_R321	Reusable	400	4
	Cabinet 02	ZXDU68 W301	R4850-1 U	4	48.6	10	40A*2, 32A*1, 25A*2, 16A*4, 10A*1	ZTE_LI_100Ah	Reusable	200	2
	Cabinet 03	APM30H	R4850GI-2U	3	52.2	5	63A*1, 16A*4	N/A	N/A	0	0
	Cabinet 04	APM30-Battery cabinet	Not Applicable	0	0	0	0	ZTE_LI_R321	Reusable	200	2
No	Task						Status				
12.2	Remarks						Cabinet 1 : Mobitel main - Battery :ZXESM R321 // Cabinet 2 : SLT - Battery :ZXESM R311 // Cabinet 3 : Mobitel 2G ODF - Rec. Module : EPW30 // Cabinet 4 : Mobitel Bat - Battery :ZXESM R321				
BBU 01											

No		Task				Status		
13.1		Cabinet No of BBU 01				Cabinet 01		
13.2		Technology of BBU 01				4G		
No	Utility	No	BBU Card	Free Port	No	BBU Card	Free Port	Utility
1	E1FANC	0	Free	N/A	4	Free		UEIU
2		1	UBBPg1	3	5	LBBPD2	6	
3		2	UBBPg3	4	6	Free		UPEUC
4		3	UBBPg1	5	7	UMPTb2		
13.4		Remarks				HW BBU3900		
BBU 02								
No		Task				Status		
14.1		Cabinet No of BBU 02				Cabinet 02		
14.2		Technology of BBU 02				4G		
No	Utility	No	BBU Card	Free Port	No	BBU Card	Free Port	Utility
1		0			4	VFC1		
2		1			5	VBPe2q	6	
3		2			6			
4		3	VPDc1		7	VSWd1		
14.4		Remarks				ZTE ZXRAN V9200		
BBU 03								
No		Task				Status		
15.1		Cabinet No of BBU 01				Cabinet 03		
15.2		Technology of BBU 01				2G		


No	Utility	No	BBU Card	Free Port	No	BBU Card	Free Port	Utility						
1		0			4									
2		1			5	GTMUb								
3		2			6	GTMUb								
4		3			7									
15.4		Remarks				HW BBU3900 // 2G (G900) - Feeder								
BBU 04														
No		Task				Status								
16.1		Cabinet No of BBU 01												
16.2		Technology of BBU 01												
No	Utility	No	BBU Card	Free Port	No	BBU Card	Free Port	Utility						
1		0			4									
2		1			5									
3		2			6									
4		3			7									
16.4		Remarks												
Antenna Details														
	Sector No	Antenna No	Antenna Type	Tower Leg	Bracket Type	Antenna Height (m)	Antenna Direction	Mechanical Tilt	Spare Port Condition	Port 01	Port 02	Port 03	Port 04	Port 05
	Sector 0	Antenna 2	8-Port Antenna	Head Frame	Single Bracket	7	0	1	Good	Free For 900	Free for 1800	Used for 2100	Free for 1800	N/A
	Sector 0	Antenna 1	20-Port Antenna	Head Frame	Single Bracket	7	0	1	With Dust Cap	Used For 900	Used for 1800	Used for 1800	Used for 2600	Used for 2600
	Sector 1	Antenna 1	20-Port Antenna	Head Frame	Single Bracket	7	120	0	With Dust Cap	Used For 900	Used for 2100	Used for 1800	Used for 2600	Used for 2600
	Sector 2	Antenna 1	20-Port Ant	Head Fram	Single Brack	7	250	1	With Dust	Used For	Used for	Used for	Used for	Used for

			enna	e	et					Cap	900	2100	1800	2600	2600		
No		Task								Status							
17.2		Remarks								Same 20P antenna used for Mobitel and SLT							
Sector Details																	
	Sect or No	Ante nna No	Sect or	Elec trica l Tilt 01	Elec trica l Tilt 02	Mec hani cal Tilt	Jum per Len gth	Jum per Con nect or Typ e	RRU Typ e	Filte r/Co mbi ner Typ e	Fee der Typ e	Fee der Con nect or	Fee der Len gth	Fibe r Co nditi on	Pow er Cabl e Co nditi on	Rem arks	
	Sect or 0	Ante nna 1	900_ A	3	N/A	1	3	DIN- DIN	DRF U	0	7 by 8	DIN	12	Goo d	N/A	Feed er	
	Sect or 0	Ante nna 1	1800 L18 00_ P	3	3	1	3	4.3-4 .3	RRU 5904 w	0	fibre	N/A	20	Goo d	Goo d	N/A	
	Sect or 0	Ante nna 1	L2.6 _sec 1	3	3	1	3	4.3-4 .3	SLT- RRU	0	fibre	N/A	20	Goo d	Goo d	RRU - N port	
	Sect or 0	Ante nna 2	UMT S_W	3	N/A	1	3	4.3- DIN	3839	0	fibre	N/A	20	Goo d	Goo d	N/A	
	Sect or 1	Ante nna 1	900_ B	3	N/A	0	3	DIN- DIN	DRF U	0	7 by 8	DIN	12	Goo d	N/A	Feed er	
	Sect or 1	Ante nna 1	1800 L18 00_ Q	3	N/A	0	3	4.3-4 .3	RRU 5904 w	0	fibre	N/A	20	Goo d	Goo d	N/A	
	Sect or 1	Ante nna 1	UMT S_X	3	N/A	0	3	4.3-4 .3	RRU 3801 C	0	fibre	N/A	20	Goo d	Goo d	2T2 R	
	Sect or 1	Ante nna 1	L2.6 _sec 2	3	3	0	3	4.3-4 .3	SLT- RRU	0	fibre	N/A	20	Goo d	Goo d	RRU - N port	
	Sect or 2	Ante nna 1	900_ C	3	N/A	1	3	DIN- DIN	DRF U	1	7 by 8	DIN	12	Goo d	N/A	Feed er // Filter avb	
	Sect	Ante	1800	4	N/A	1	3	4.3-4	Othe	0	fibre	N/A	20	Goo	Goo	RRU	


	or 2	nna 1	L18 00_ R					.3	r2					d	d	5867
	Sect or 2	Ante nna 1	UMT S_Y	4	N/A	1	3	4.3-4 .3	Othe r2	0	fibre	N/A	20	Goo d	Goo d	RRU 5867
	Sect or 2	Ante nna 1	L2.6 _sec 3	3	3	1	3	4.3-4 .3	SLT- RRU	0	fibre	N/A	20	Goo d	Goo d	RRU - N port
No		Task								Status						
18.2		Remarks														
Existing Site Photo Proof Mobitel																
Mobitel Overall Site View									Mobitel Overall Site View 2							
Mobitel Overall Site View 3									Mobitel Aerial View 1							
Mobitel Aerial View 2									Mobitel Aerial View 3							
Mobitel Aerial View 4									Mobitel Exiting Tower View							
Mobitel Existing Equipment detail Outlook									Mobitel Existing Equipment detail Outlook 2							
Mobitel Existing Equipment detail In look									Mobitel Existing Equipment detail In look 2							
Mobitel Existing Equipment detail In look 3									Mobitel Existing Equipment detail In look 4							

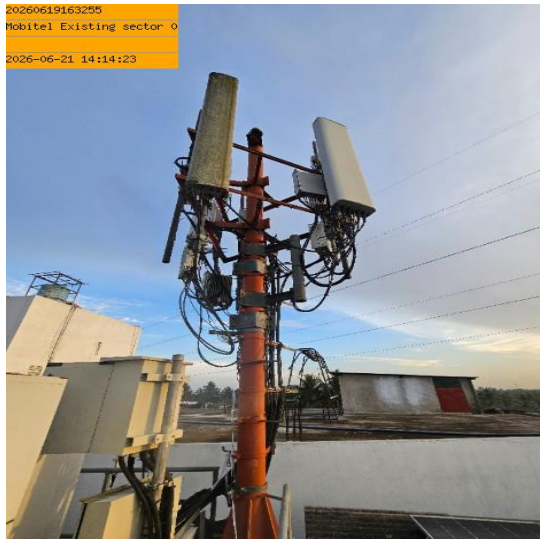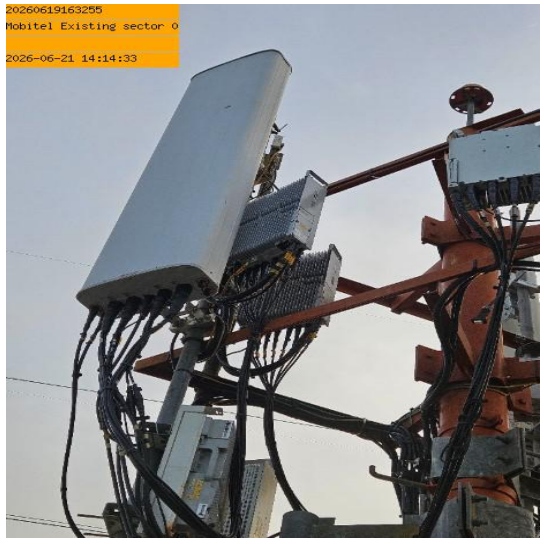Mobitel Existing foot print (Back side of the plinth)	Mobitel Existing BBU
Mobitel Existing Batteries	Mobitel Existing Batteries 2
Mobitel Existing Batteries 3	Mobitel Existing sector 01(Overall picture) 20260619163255 Mobitel Existing sector 0 2026-06-21 14:14:23 
Mobitel Existing sector 02(Overall picture) 20260619163255 Mobitel Existing sector 0 2026-06-21 14:14:28 	Mobitel Existing sector 03 (Overall picture) 20260619163255 Mobitel Existing sector 0 2026-06-21 14:14:33 


Mobitel Existing RF antenna sector 01

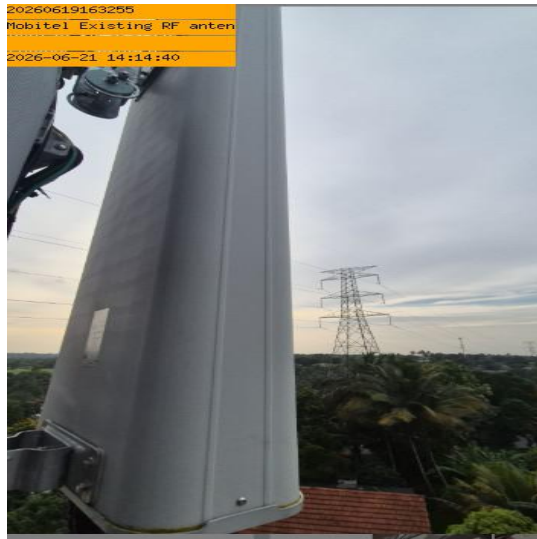

Mobitel Existing RF antenna sector 02

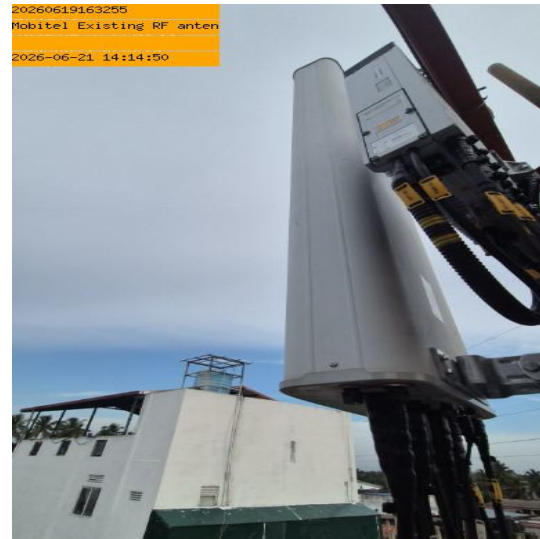

Mobitel Existing RF antenna sector 03

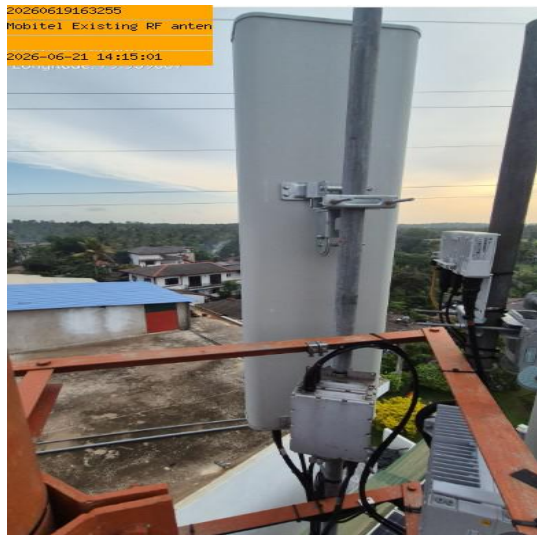

Mobitel Existing RF antenna azimuth sector 01




Mobitel Existing RF antenna azimuth sector 02



Mobitel Existing RF antenna azimuth sector 03




Mobitel Existing RF antenna Bottom View sector 01

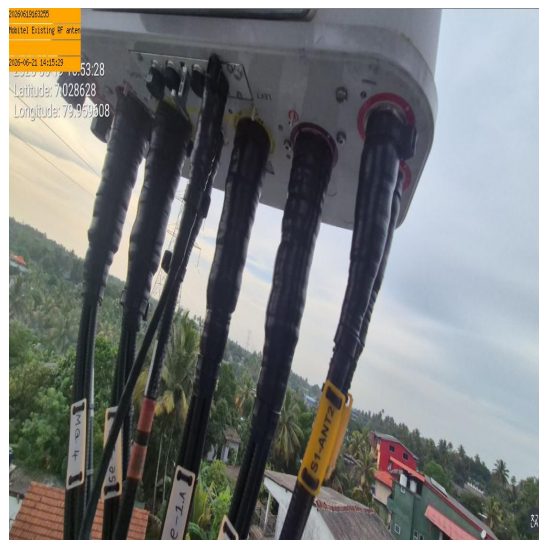

Mobitel Existing RF antenna Bottom View sector 02




Mobitel Existing RF antenna Bottom View sector 03

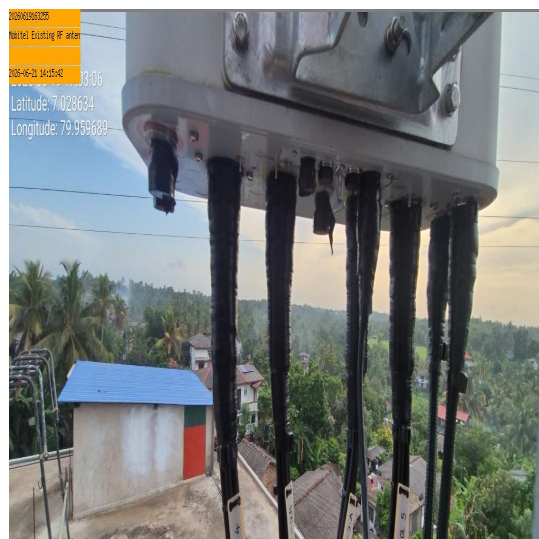

Mobitel Existing RRU Sector 01




Mobitel Existing RRU Sector 01 image2

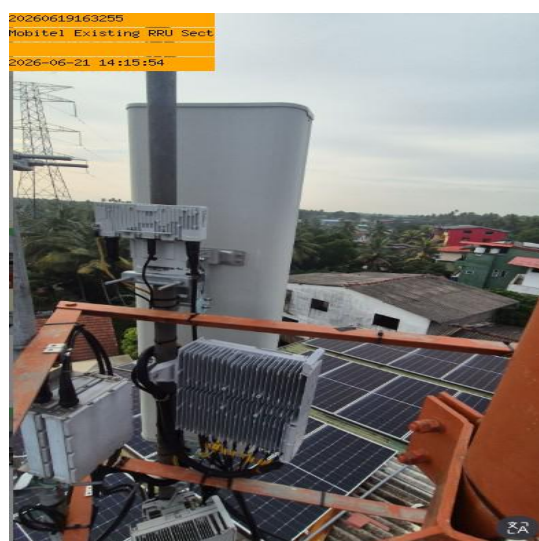

Mobitel Existing RRU Sector 02



Mobitel Existing RRU Sector 02 image2

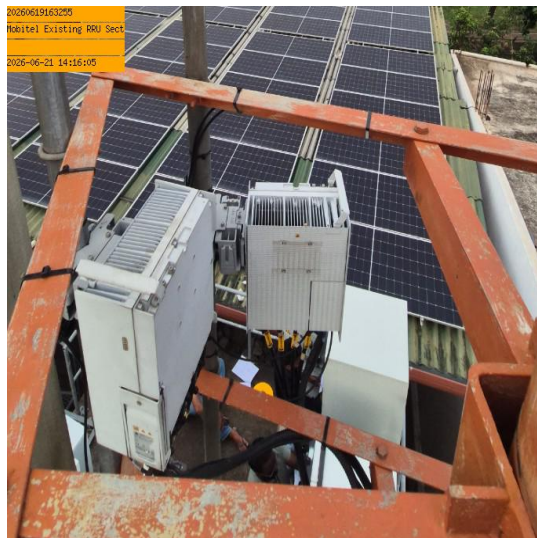

Mobitel Existing RRU Sector 03



Mobitel Existing RRU Sector 03 image2





Mobitel Existing cable ladder (Vertical)




Mobitel Existing cable ladder (Vertical) image2

Mobitel Existing cable ladder (Horizontal)


Mobitel Existing cable ladder (Horizontal) image2	Mobitel Location for Mobitel Equipment
Mobitel Location for Power Source	Mobitel Cable Entry Port Photo
Mobitel Existing Meter (Close Up)	Mobitel Stairs, Elevator and Other Entries
Mobitel All ECB connection point	Mobitel ECB connection point 1
Mobitel ECB connection point 2	Mobitel Existing GPS antenna
Mobitel Evidence for special manual transport	Mobitel Evidence for special manual transport 2
Mobitel Special Photos to highlight issues (if any)	Mobitel Special Photos to highlight issues (if any) 2
Existing Site Photo Proof SLT	
SLT Overall Site View	SLT Overall Site View 2
SLT Overall Site View 3	SLT Aerial View 1
SLT Aerial View 2	SLT Aerial View 3
SLT Aerial View 4	SLT Exiting Tower View
SLT Existing Equipment detail Outlook	SLT Existing Equipment detail Outlook 2

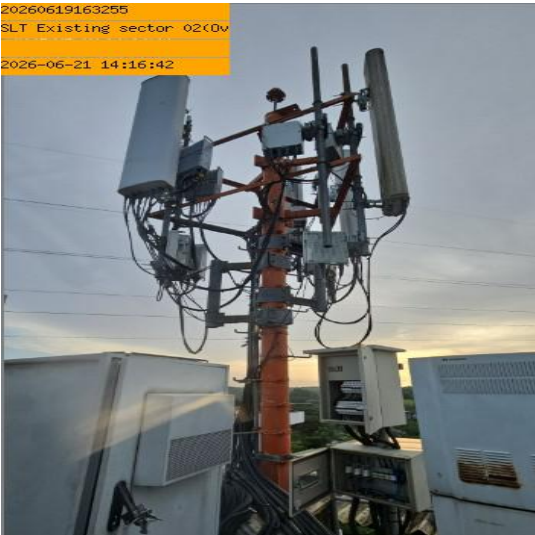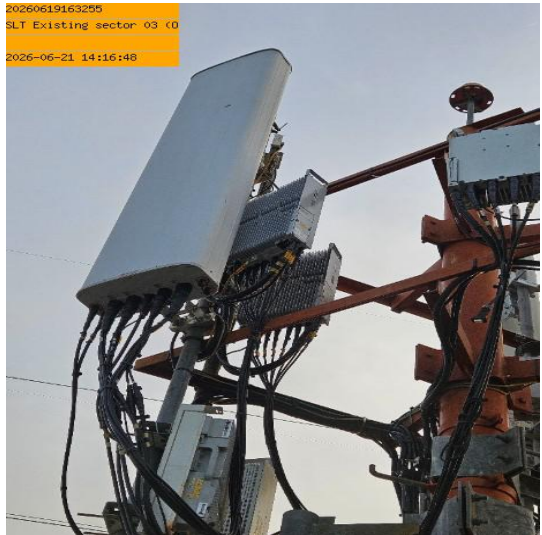SLT Existing Equipment detail In look	SLT Existing Equipment detail In look 2
SLT Existing Equipment detail In look 3	SLT Existing Equipment detail In look 4
SLT Existing foot print (Back side of the plinth)	SLT Existing BBU
SLT Existing Batteries	SLT Existing Batteries 2
SLT Existing Batteries 3	SLT Existing sector 01(Overall picture) 
SLT Existing sector 02(Overall picture) 	SLT Existing sector 03 (Overall picture) 

SLT Existing RF antenna sector 01

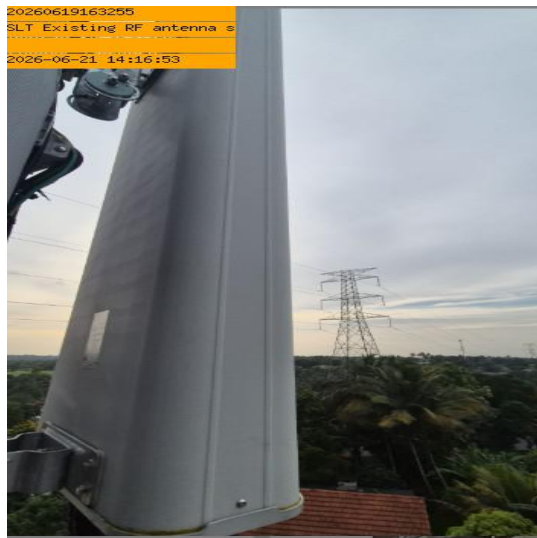

SLT Existing RF antenna sector 02

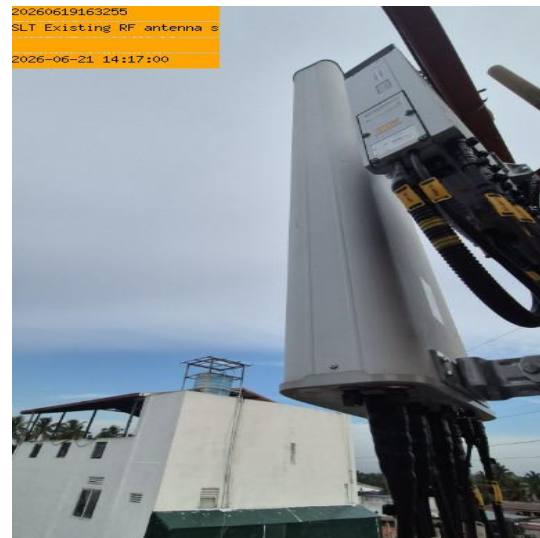

SLT Existing RF antenna sector 03



SLT Existing RF antenna azimuth sector 01




SLT Existing RF antenna azimuth sector 02



SLT Existing RF antenna azimuth sector 03




SLT Existing RF antenna Bottom View sector 01

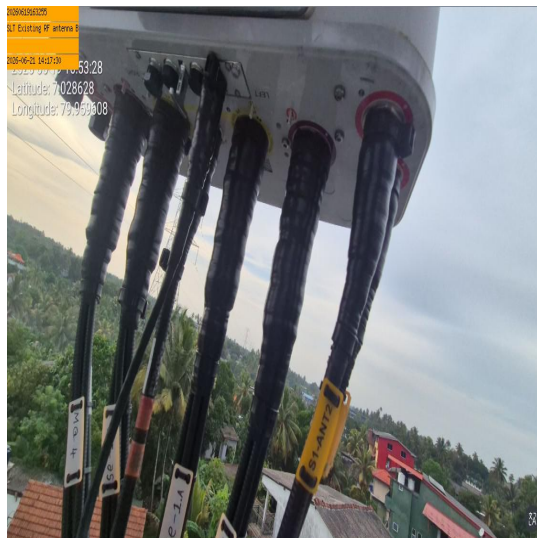

SLT Existing RF antenna Bottom View sector 02



SLT Existing RF antenna Bottom View sector 03

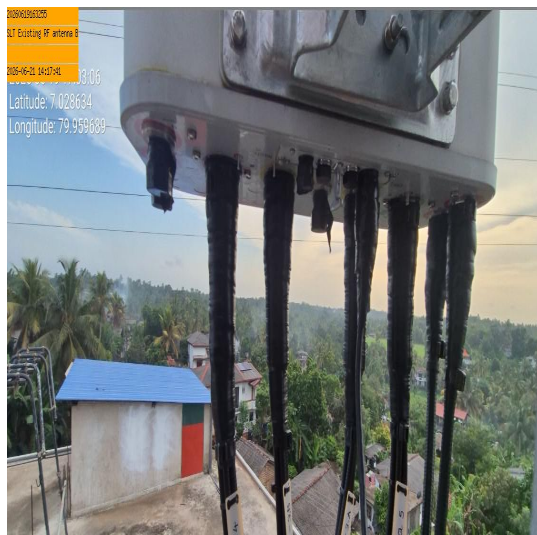

SLT Existing RRU Sector 01



SLT Existing RRU Sector 02



SLT Existing RRU Sector 03



SLT Existing cable ladder (Vertical)						SLT Existing cable ladder (Vertical) image2							
SLT Existing cable ladder (Horizontal)						SLT Existing cable ladder (Horizontal) image2							
SLT Location for SLT Equipment						SLT Location for Power Source							
SLT Cable Entry Port Photo						SLT Existing Meter (Close Up)							
SLT Stairs, Elevator and Other Entries						SLT All ECB connection point							
SLT ECB connection point 1						SLT ECB connection point 2							
SLT Existing GPS antenna						SLT Evidence for special manual transport							
SLT Evidence for special manual transport 2													
Solution Cabinet Info													
No		Task						Status					
21.1		Solution Type						Huawei ZTE swap with 5G addition					
21.2		Overall solution, scope with special comments						1st Ex.Mobitel indoor ODF need to cut over to out side.Can use Ex.SLT cabinet for new UPG.Ex.Mobitel ATN need to relocate at SLT cabinet.Need to install new DCDCU for other RRU power.Need to Remove All Antenna & Huawei RRU, Pro,New 16-Port Antenna at all sectors.SLT L2.6 RRU need to connect new antenna./// Sec0 & Sec2 need to add R9264H RRU for G9L18L21(L18 4T4R) & R9264 M1821N(L18 4T4R) for Dual Beam port/// Sec1 need to add R9264H RRU for G9L18L21. .///Pro new 900 filter for all sectors.///No free space at casing installation.///Ex-G900 feeder system need to remove. Finally need to remove all Huawei cabinet,No space to manual handling,Need crane operation for cabinet RMV-(Long arm crane).Need Regional feedback for this issue					
21.3		Proposed Equipment Type						Outdoor					
21.4		Enough Space for Cabinet						Yes					
21.5		Enough Space for BBU Cards						No					
21.6		Enough Space for DCDCU						No					
Cabine t No	Cabine t Type	Rectifi er type	Rectifi er Qty	DC Volutag e	Spare Breake r Qty	Spare Breake r Capaci	Battery Type	Battery Physic al Con dition	Battery Capaci ty	Battery Qty	Cabine t Status		

							ty						
	Cabinet 01	TP4820 0A	R4850-1U	2	51.1	3	63A*1, 16A*2	ZTE_LI_R321	Reusab le	400	4	Remov ed	
	Cabinet 02	ZXDU6 8 W301	R4850-1U	4	48.6	10	40A*2, 32A*1, 25A*2, 16A*4, 10A*1	ZTE_LI_100Ah	Reusab le	200	2	Live	
	Cabinet 03	APM30 H	R4850 GI-2U	3	52.2	5	63A*1, 16A*4	N/A	N/A	0	0	Remov ed	
	Cabinet 04	APM30 -Battery cabinet	Not Ap plicable	0	0	0	0	ZTE_LI_R321	Reusab le	200	2	Remov ed	
21.8		Remarks						Propose to Remove all huawei cabinet					
Solution BBU 01													
No		Task						Status					
22.1		Solution BBU 01 Status						Removed					
No	Utility		No	BBU Card		Free Port		No	BBU Card		Free Port		Utility
1	E1FANC		0	Free		N/A		4	Free				UEIU
2			1	UBBPg1		3		5	LBBPD2		6		
3			2	UBBPg3		4		6	Free				UPEUC
4			3	UBBPg1		5		7	UMPTb2				
22.3		Remarks											
Solution BBU 02													
No		Task						Status					
23.1		Solution BBU 02 Status						Live					
No	Utility		No	BBU Card		Free Port		No	BBU Card		Free Port		Utility
1			3	VPDc1				7	VSWd1				
2			1					5	VBPe2q		6		
3			0					4	VFC1				

4		2			6									
23.3	Remarks				need to add VBPe3p card for Mobitel CPRI									
Solution BBU 03														
No	Task				Status									
24.1	Solution BBU 03 Status													
No	Utility	No	BBU Card	Free Port	No	BBU Card	Free Port	Utility						
1		1			5	GTMUb								
2		2			6	GTMUb								
3		0			4									
4		3			7									
24.3	Remarks													
Solution BBU 04														
No	Task				Status									
25.1	Solution BBU 04 Status													
No	Utility	No	BBU Card	Free Port	No	BBU Card	Free Port	Utility						
1		0			4									
2		1			5									
3		2			6									
4		3			7									
25.3	Remarks													
Solution Antenna Details														
	Sector No	Antenna No	Antenna Type	Tower Leg	Bracket Type	Antenna Height (m)	Antenna Direction	Mechanical Tilt	Spare Port Condition	Port 01	Port 02	Port 03	Port 04	Port 05
	Sector 0	Antenna 1	20-Port Antenna	Head Frame	Single Bracket	7	0	1	With Dust Cap	Used For 900	Used for 1800	Used for 1800	Used for 2600	Used for 2600
	Sector 1	Antenna 2	8-Port _Antenna	Head Frame	Single Bracket	7	0	1	Good	Free For	Free for	Used for	Free for	N/A

			nna	e	et						900	1800	2100	1800		
	Secto r 1	Anten na 2	8-Port _Ante nna	Head Fram e	Single Brack et	7	0	1	Good	Free For 900	Free for 1800	Used for 2100	Free for 1800	N/A		
		Anten na 1	20-Po rt Ant enna	Head Fram e	Single Brack et	7	0	1	With Dust Cap	Used For 900	Used for 1800	Used for 1800	Used for 2600	Used for 2600		
	Secto r 1	Anten na 1	20-Po rt Ant enna	Head Fram e	Single Brack et	7	120	0	With Dust Cap	Used For 900	Used for 2100	Used for 1800	Used for 2600	Used for 2600		
	Secto r 2	Anten na 1	20-Po rt Ant enna	Head Fram e	Single Brack et	7	250	1	With Dust Cap	Used For 900	Used for 2100	Used for 1800	Used for 2600	Used for 2600		
No		Task							Status							
26.2		Remarks														
Solution Sector Details																
	Sect or No	Ante nna No	Sect or	Elec trica l Tilt 01	Elec trica l Tilt 02	Mec hani cal Tilt	Jum per Len gth	Jum per Con nect or Typ e	RRU Typ e	Filte r/Co mbi ner Typ e	Fee der Typ e	Fee der Con nect or	Fee der Len gth	Fibe r Co nditi on	Pow er Cabl e Co nditi on	Rem arks
	Sect or 0	Ante nna 1	900_ A	3	N/A	1	3	DIN- DIN	DRF U	0	7 by 8	DIN	12	Goo d	N/A	Feed er
	Sect or 0	Ante nna 1	900_ A	3	N/A	1	3	DIN- DIN	DRF U	0	7 by 8	DIN	12	Goo d	N/A	Feed er
	Sect or 0	Ante nna 1	1800 L18 00_ P	3	3	1	3	4.3-4 .3	RRU 5904 w	0	fibre	N/A	20	Goo d	Goo d	N/A
	Sect or 0	Ante nna 1	L2.6 _sec 1	3	3	1	3	4.3-4 .3	SLT- RRU	0	fibre	N/A	20	Goo d	Goo d	RRU - N port
	Sect or 0	Ante nna 2	UMT S_W	3	N/A	1	3	4.3- DIN	3839	0	fibre	N/A	20	Goo d	Goo d	N/A
	Sect	Ante	900_ A	3	N/A	0	3	DIN- DIN	DRF U	0	7 by 8	DIN	12	Goo d	N/A	Feed er

	or 1	anna 1	B					DIN	U		8			d		er
	Sect or 1	Ante nna 1	1800 L18 00_ Q	3	N/A	0	3	4.3-4 .3	RRU 5904 w	0	fibre	N/A	20	Goo d	Goo d	N/A
	Sect or 1	Ante nna 1	UMT S_X	3	N/A	0	3	4.3-4 .3	RRU 3801 C	0	fibre	N/A	20	Goo d	Goo d	2T2 R
	Sect or 1	Ante nna 1	L2.6 _sec 2	3	3	0	3	4.3-4 .3	SLT- RRU	0	fibre	N/A	20	Goo d	Goo d	RRU - N port
	Sect or 2	Ante nna 1	900_ C	3	N/A	1	3	DIN- DIN	DRF U	1	7 by 8	DIN	12	Goo d	N/A	Feed er // Filter avb
	Sect or 2	Ante nna 1	1800 L18 00_ R	4	N/A	1	3	4.3-4 .3	Othe r2	0	fibre	N/A	20	Goo d	Goo d	RRU 5867
	Sect or 2	Ante nna 1	UMT S_Y	4	N/A	1	3	4.3-4 .3	Othe r2	0	fibre	N/A	20	Goo d	Goo d	RRU 5867
	Sect or 2	Ante nna 1	L2.6 _sec 3	3	3	1	3	4.3-4 .3	SLT- RRU	0	fibre	N/A	20	Goo d	Goo d	RRU - N port

No	Task	Status
27.2	Remarks	

Solution MCW Info							
-------------------	--	--	--	--	--	--	--

No	Name	Requirment	Type	Location/direc tion Qty	Space available	Approval Available	Comments
1	Plinth 1						
2	Plinth 2						
3	Plinth 3						
4	Bracket 1						
5	Bracket 2						

6	Bracket 3						
7	Bracket 4						
8	Bracket 5						
9	Bracket 6						
10	Extension bar (Horizontal)						
11	Extension bar (Vertical)	Yes	UV Type	Mobitel Horizontal ladder	Yes	N/A	No space for casin installation
12	Ladder (Horizontal)						
13	Ladder (Vertical)						
No		Task			Status		
28.2		MCW Solution Remarks			No space for casin installation		
Solution Power Info							
No		Task			Status		
29.1		Power Upgrade Required			No		
29.2		Power Upgrade need Phase					
29.3		Power Upgrade remarks			Use Existing Mobitel MC,SPD & ACDP// Can use Ex, SLT Battery bank//Need to install new DCDU-Total Power-11		
No	Name	Requirment	Type	Location/direction Qty	Space available	Approval Available	Comments
1	SPD						
2	ACDB						
3	Meter Cubicle						
4	Additional ECBs						
5	ECB Earth Cable						
6	Meter To ACDB Power Cable Length (4X16mm2) (m)						
7	RRU Power Cable Length (m)	Yes	2x10m	DCDU to RRU	Yes	Yes	N/A


8	RRU Ground Cable Length (m)	Yes	16m	RRU to tower ECB	Yes	Yes	N/A
9	DCDU power cable length (m)						
10	ACDB Ground Cable Length (25 mm2) (m)						
11	Battety Cabinet Ground Cable Length (25 mm2) (m)						
12	BTS and BBU Ground Cable Length (25mm2) (m)						
13	SPD Pole Ground Cable Length (35 mm2) (m)						
14	GI Pipe from ACDB to BTS (m)						
15	PVC Pipe from the BTS to RRU (fiber & Power) (m)	Yes	20	Horizontal & vertical cable path	Yes	Yes	N/A

Material Requirment

No	Generic Name	ERP Code	UOM	Qty (Option 01)	Qty (Option 02)	Comments
1	VBBP	ZT-VBBPe3p		Each	1	1
2	DCPD-10	ZT-DCPD10B		Each	1	1
3	RRU-AAU	SP-ZT-AAU-A9652-S35		Each	3	3
4	RRU-AAU	SP-ZT-RRU9264H-M901821		Each	3	3
5	RRU-AAU	SP-ZT-RRU9264-M1821 N		Each	2	2
6	SMR	ZT-SMR3000-V6		Each	5	5
7	900 Filter	SP-ZT-COMBINE R-FL8590A		Each	3	3
8	Antenna	SP-ZT-SEC-ANTE NNA-16PORT		Each	3	3

9	Battery	SLT-ZT-LIFE-BAT48V100AH		Each	2	2
10	Fibre length - per fibre (m)	ZT-OPTICAL-CABLE-SM-20MÂ		Each	8	8
11	Fibre clamp	OPHU27150063		Each	50	50
12	No. of RRU DC power cable	ZT-PAD-PWR-OUT-CABLE-2X10MM2		Each	8	8
13	RRU DC power cable length (m)	ZT-RRUDCCABLE-2X10MM2_UOM(m)		Meter	100	100
14	RRU DC power cable length (m)	PWZTNARMOUR DC2X16MM		Meter	60	60
15	Cable extension bar	IMEXTNBARZT		Each	2	2
16	16mm2 earth cable (m)	PRZT052521000129		Meter	28	28
17	25mm2 DC cable (Black) (m)	PW-CABLE-25MM 2-DC-BLACK		Meter	5	5
18	25mm2 DC cable (Blue) (m)	PW-CABLE-25MM 2-DC-BLUE		Meter	5	5
19	16mm2 DC cable (m)	PW-CABLE-16MM 2-DC-BLACK		Meter	4	4
20	GI coated flexible 32mm (m)	UN-GIFLEXIBLE-PVCINSULATE-3/4		Meter	100	100
21	PVC pipe 20mm (m)	UN-PVC-PIPE-20mm		Meter	65	65
22	PVC casing 4x4 (m)	UN-PVC-CASING		Meter	6	6
23	Jumper cable (3m)	UN-DM-DM-S-JUMPER-3M[22-22]		Each	26	26
24	Ethernet cable (m)	PRHU04070012		Meter	10	10
25	SFP module RRU side (Single-mode)	ZT-SFP-SM-10G_F		Each	5	5
26	SFP module BBU side (Single-mode)	ZT-SFP-SM-10G_F		Each	5	5
27	Optical fibre cable (Single-mode)	ZT-OPTICAL-CABLE-SM-20MÂ		Each	8	8
28	For TX: No. of patch cord (Single mode LC-LC)	TXOCABLE_LCLC SM10MT		Each	2	2
29	For TX: Patch cord	TXOCABLE_LCF		Each	2	2

	length (m)	CSM10MT				
30	Other	ZT-SFP-25G		Each	6	6
31	Other	ZT-RRU-INSKIT		Each	8	8
32	Other	OPZTB8200L200		Each	10	10
Proposed Solution Photos						
Sketch List						
Punch List						
No	Task			Status		
33.1	Punch List 01					
33.2	Punch List 02					
33.3	Punch List 03					
33.4	Punch List 04					
33.5	Punch List 05					
Modification Request						
No	Task			Status		
34.1	Modification Request 01					
34.2	Modification Request 02					
34.3	Modification Request 03					
34.4	Modification Request 04					
34.5	Modification Request 05					
Approval						
No	Task			Status		
35.1	TSSR Status					
35.2	Process Flow					
35.3	Reassign Officer					
35.4	Final Approval Remarks					



Performed By	Nuwan Chathuranga	2026-06-21 14:53:01
--------------	-------------------	---------------------
